

The background of the slide features a large, faded seal of Williamson County, Tennessee. The seal is circular with a blue border containing the text "WILLIAMSON COUNTY" at the top and "TENNESSEE" at the bottom, separated by two stars. The central shield is divided into four quadrants: top-left (red) with a white plow, top-right (red) with a white sheaf of wheat, bottom-left (green) with a white open book and a cross, and bottom-right (green) with a brown horse and a brown cow. A dark teal horizontal bar is at the top of the slide.

*JAIL, JUVENILE JUSTICE CENTER, &  
ALTERNATIVE LEARNING CENTER*

# MONTHLY REPORT

FEBRUARY 2025



PREPARED BY  
Oversite

# CONTENTS



---

**1**  
ALTERNATIVE LEARNING CENTER PROJECT UPDATES

---

**2**  
JAIL PROJECT UPDATES

---

**3**  
JUVENILE JUSTICE CENTER UPDATES

---

**4 - 6**  
JJJ PROJECT SCHEDULE

### ALTERNATIVE LEARNING CENTER

- WC JJJ project team meeting to establish expectations on schedule for all JJJ projects including the Jail, Juvenile Justice Center, Alternative Learning Center, Gun Range, and Impound Lot.
- WC JJJ project team met with ALC stakeholders to achieve the below goals:
- identify needed program updates.
- confirm that the existing program supports priorities for community, youth, and staff spaces.
- identify program efficiencies to help reduce the overall square footage of the ALC.
- Review possible “re-design” layouts of the ALC being a re-use of the 300 Beasley warehouse.
- review schematic “re-design” schedule and ways to improve this schedule.
- Schedule meetings over the next few months to review Schematic Design “check points” with stakeholders.
- Design team continued progressing through Schematic Design drawings.


## JAIL

- WC JJJ project team meeting to establish expectations on schedule for all JJJ projects including the Jail, Juvenile Justice Center, Alternative Learning Center, Gun Range, and Impound Lot.
- WC JJJ project team met with Jail, Sheriff's Office, Gun Range, and Impound Lot stakeholders to achieve the below goals:
- identify needed program updates.
- confirm that the existing program supports priorities for Sheriff's office, Jail staff, and John Coyle's teams needs.
- Review site logistics and update Sheriff's teams on possible utility improvements due to JJC and ALC changes.
- Review design development schedule and ways to improve this schedule.
- Review different construction methods with Bell to analyze cost benefits.
- Made changes to Gun Range to improve efficiencies in this space as well as save cost.
- Schedule meetings over the next few months to review design "check points" with stakeholders, specifically looking at reviewing current DD design, finding additional efficiencies to minimize square footage needs, and reviewing different construction methods dependent on cost.
- Seismic monitoring was completed and the report was distributed to Oversight. The seismic report is included in this project update.
- Design Team continued progressing through Design Development drawings.

### JUVENILE JUSTICE CENTER

- WC JJJ project team meeting to establish expectations on schedule for all JJJ projects including the Jail, Juvenile Justice Center, Alternative Learning Center, Gun Range, and Impound Lot.
- WC JJJ project team met with JJC stakeholders to achieve the below goals:
- identify needed program updates.
- confirm that the existing program supports priorities for community, youth, and staff spaces.
- identify program efficiencies to help reduce the overall square footage of the JJC.
- Review possible “re-design” layouts of the JJC due to detaching the ALC.
- review schematic “re-design” schedule and ways to improve this schedule.
- Schedule meetings over the next few months to review Schematic Design “check points” with stakeholders.
- Design team continued progressing through Schematic Design drawings.


PROJECT SCHEDULE

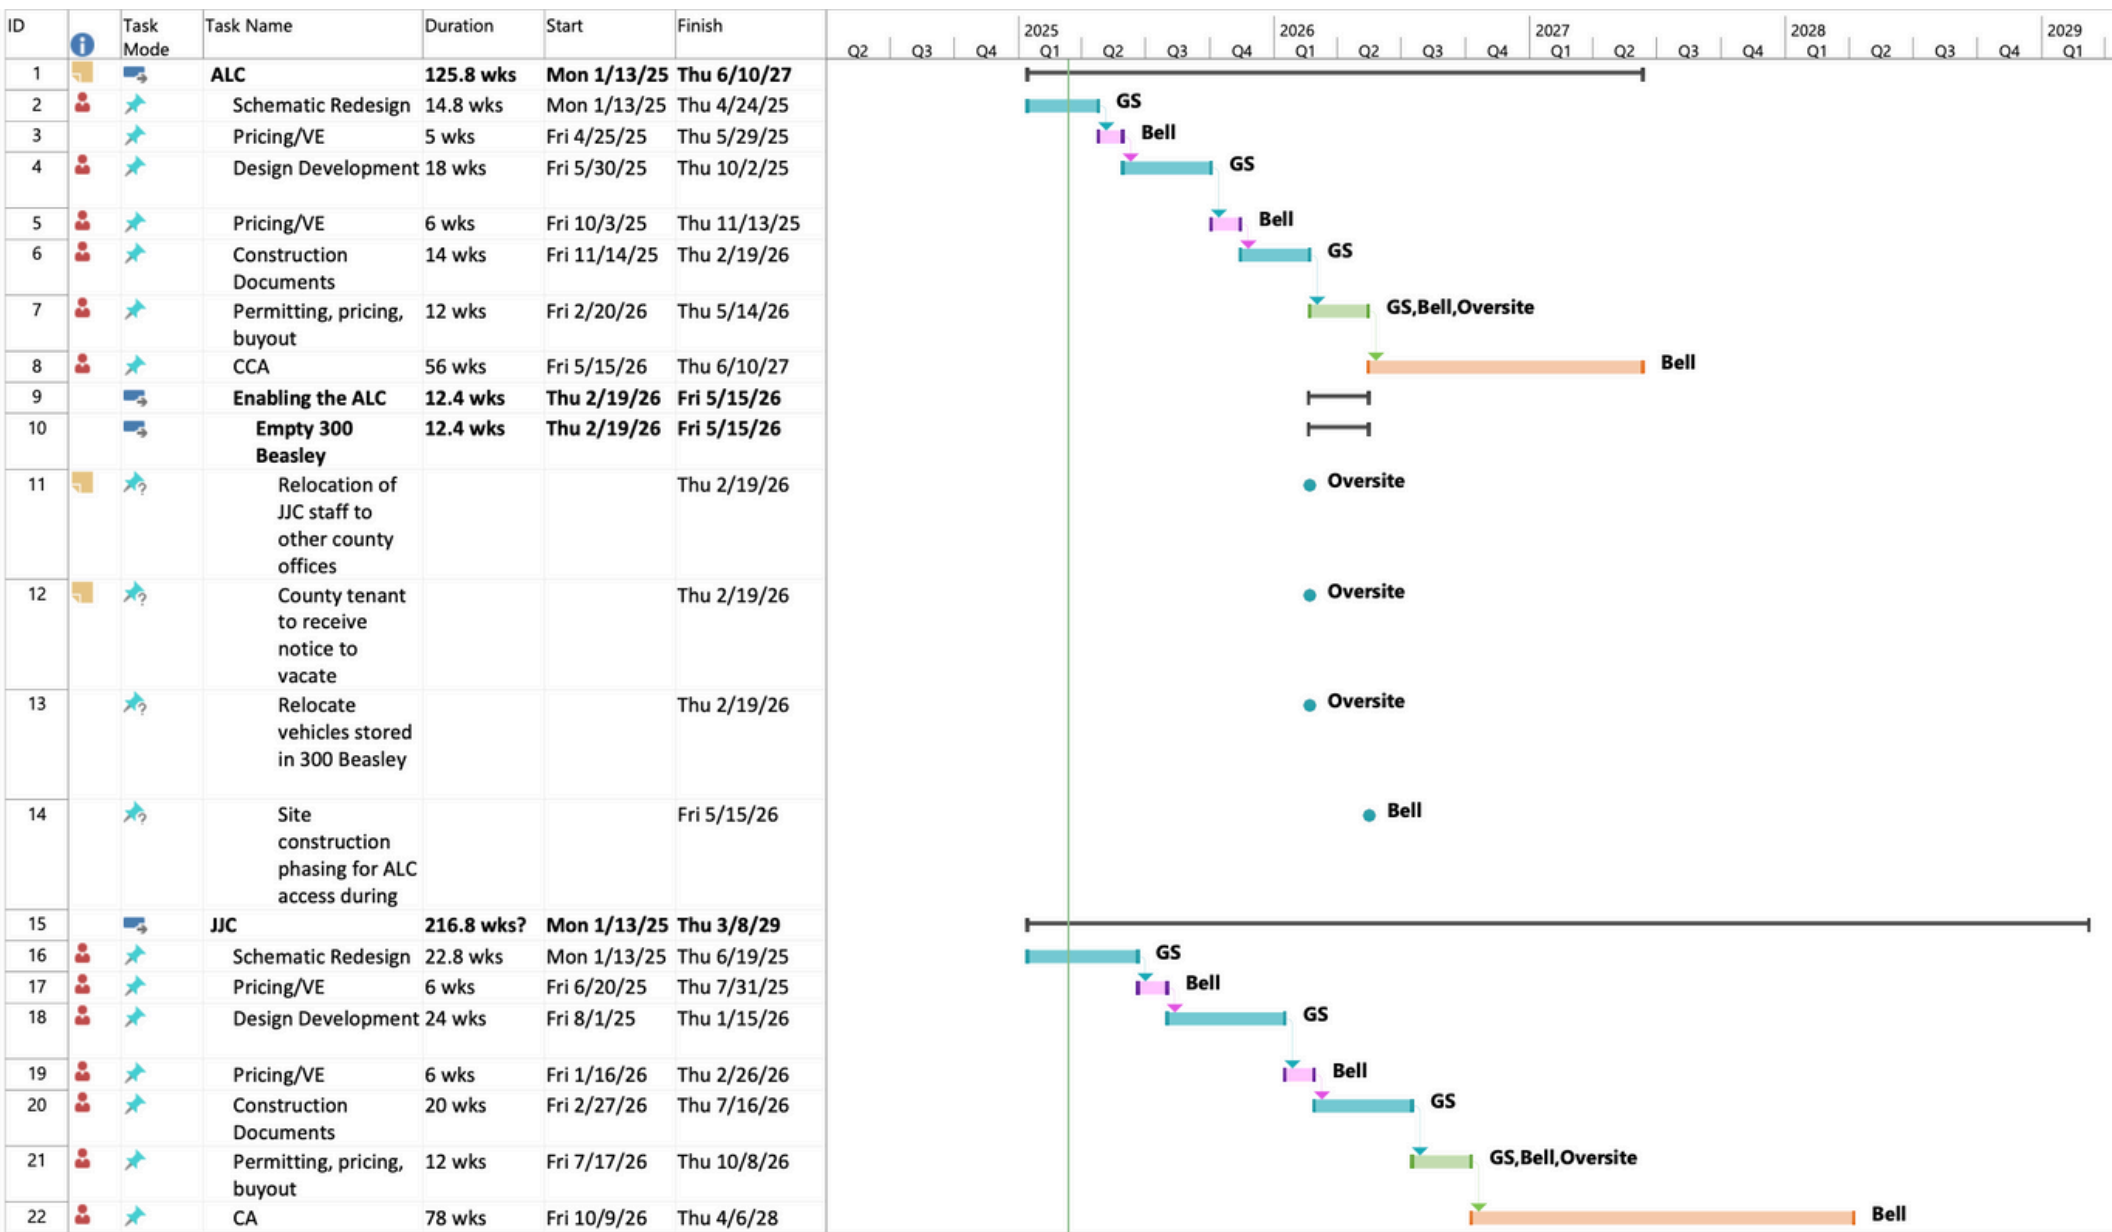

Project: Simple Project Plan  
Date: Thu 3/13/25

Task	<div></div>	Project Summary	<div></div>	Manual Task	<div></div>	Start-only	<div></div>	Deadline	<div></div>
Split	<div></div>	Inactive Task	<div></div>	Duration-only	<div></div>	Finish-only	<div></div>	Progress	<div></div>
Milestone	<div></div>	Inactive Milestone	<div></div>	Manual Summary Rollup	<div></div>	External Tasks	<div></div>	Manual Progress	<div></div>
Summary	<div></div>	Inactive Summary	<div></div>	Manual Summary	<div></div>	External Milestone	<div></div>		

# PROJECT SCHEDULE

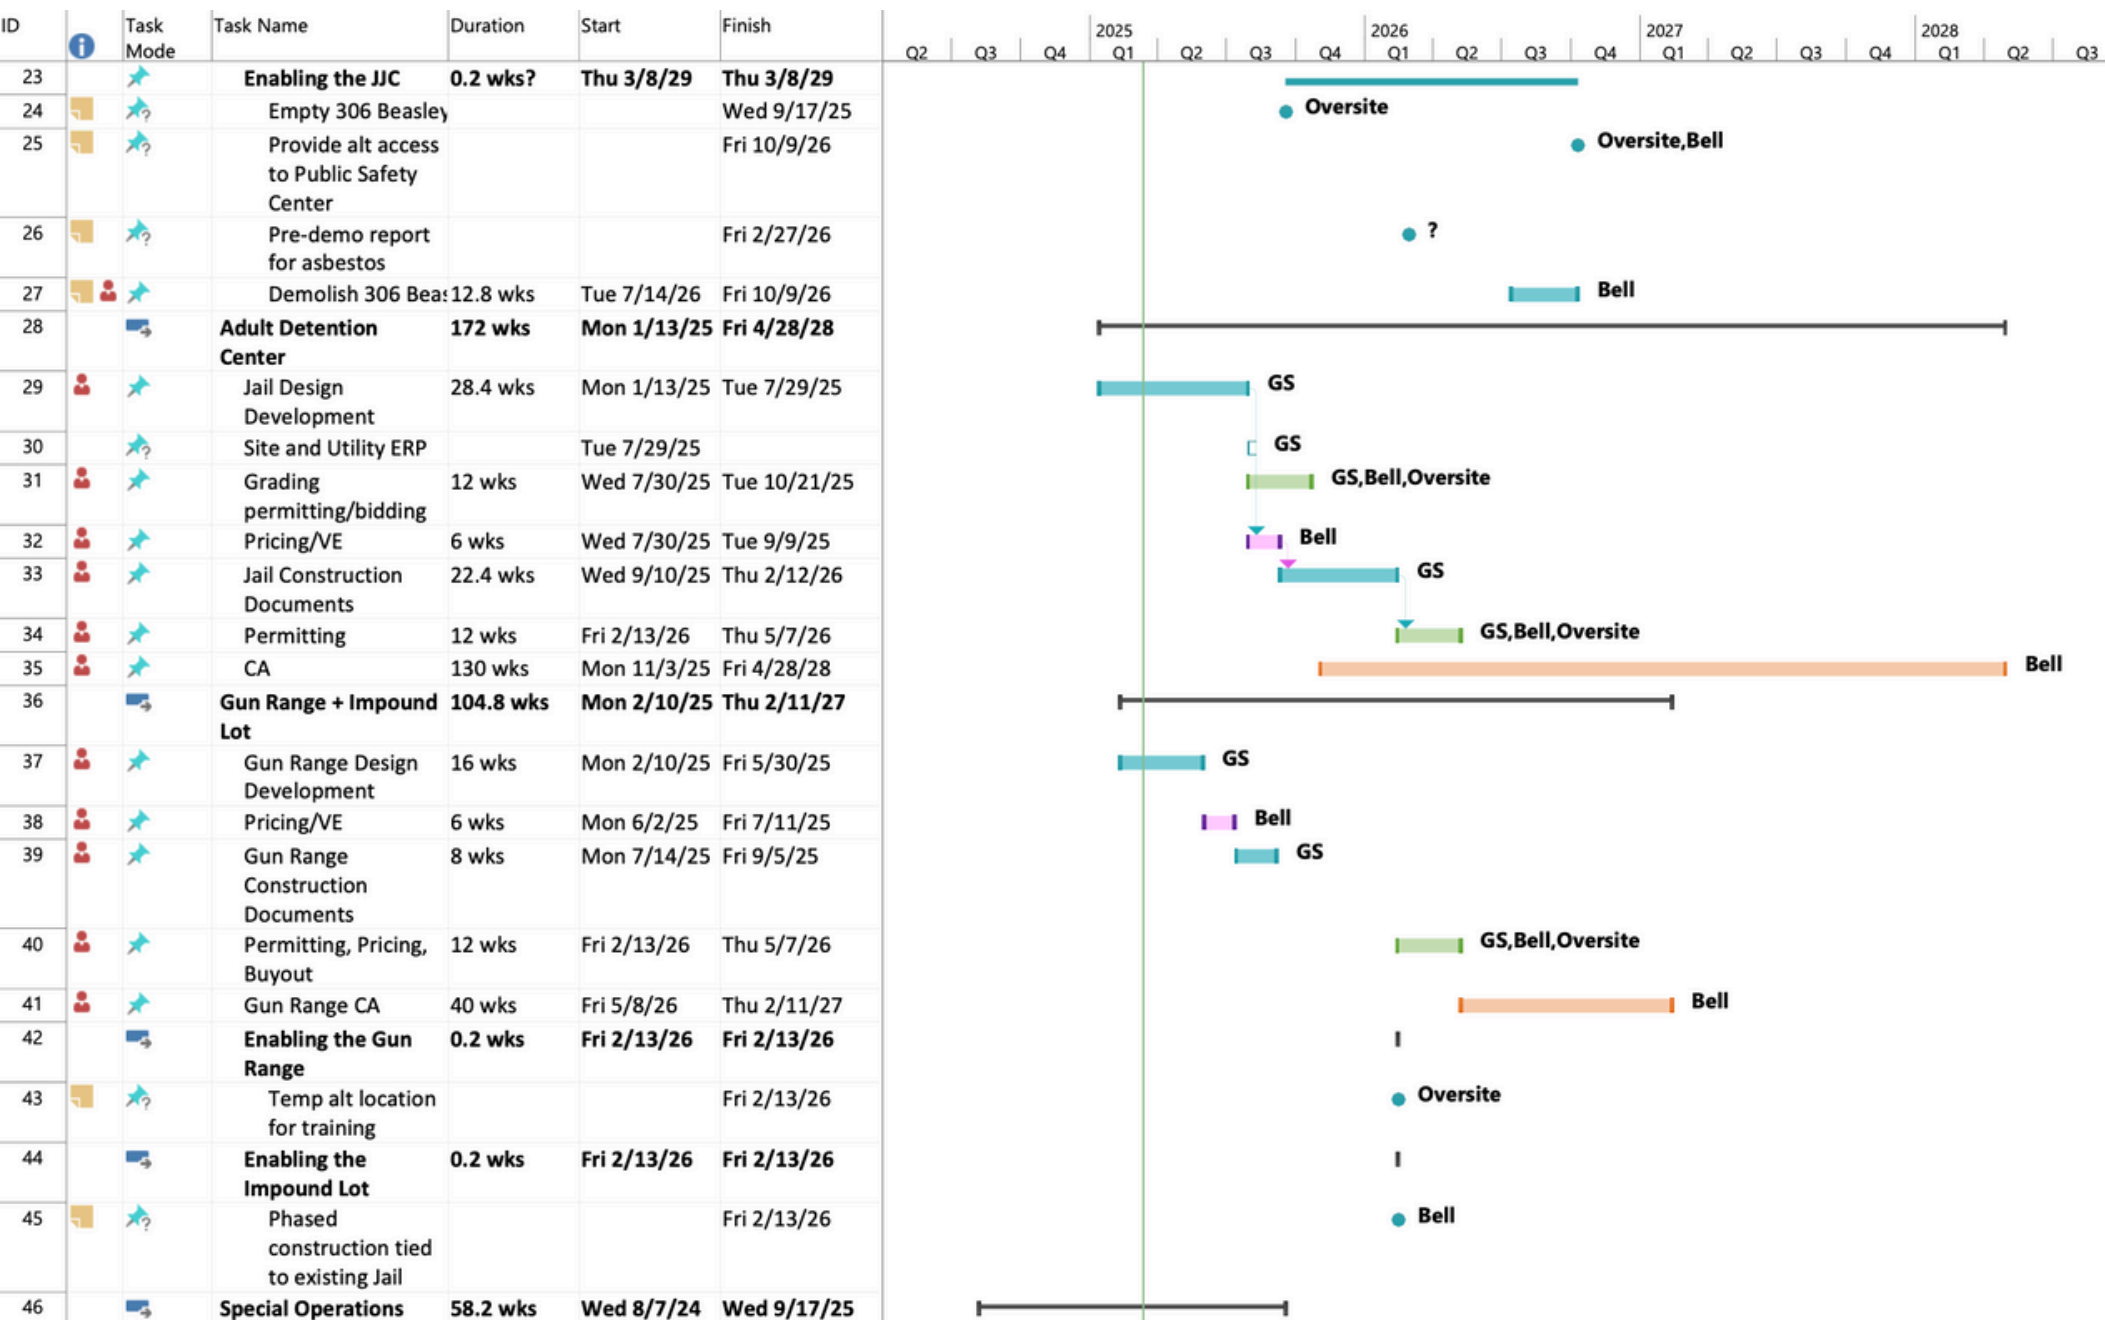

# PROJECT SCHEDULE

